

## Bond Projects Updates for Monday 1 July 2013

### Community Center

- Sump pump pit passed soils inspection and sleeve was set.
- Roofing base layer completed.
- Storefront window and door framing nearly completed.
- HVAC packages installed on roof.
- Interior insulation (roof/ceiling) installation continued.
- Lath and paper installation continued in preparation for stucco finish.



Storefront framing at the main events entry. (20130628-0826)



East end of the Perera Pavilion has its storefront framing installed. ((20130628-0833)




Dry fit for the sump pump housing, just prior to a soils moisture and compaction test. Kitchen entrance door seen at top of photo.

(20130628-0824)

Installing metal trim elements, south side of events room.

(20130628-0830)

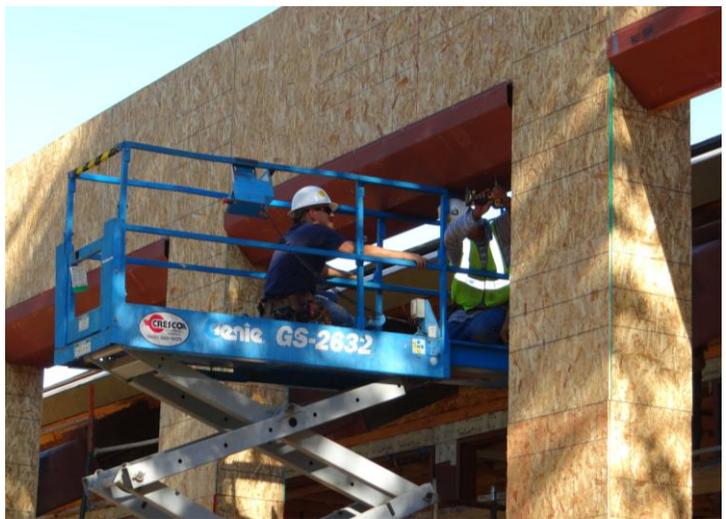

Lifting an HVAC unit over the preschool rooms. (20130628-0953)



Good progress on the roof “paper”, and lath and paper for the stucco. (20130628-1012)



The 40 ton Bigge crane lifting HVAC units to the roof for the kitchen, restrooms, and events room.

This was the second location for lifting the units, which provided protective clearance for the Valley Oak at the front of the building.

(20130628-1043)

Pleasant Oaks Park

- Grading, grading, grading...
- Delivery of irrigation and drainage material.



“Purple Pipe” is designated for reclaimed water for irrigation, while white pipe is for potable water, used in the snack shack, restroom sinks, and drinking fountains. (20130627-1014 )



Above and below: Staging some irrigation and drainage materials. (20130627-1014)

