


Bond Projects Updates for Monday 10 December 2012

Senior Center

- Monument sign base was poured – sign installation planned in this upcoming week.
- Exterior way-finding signs were installed throughout the project sites.
- Operable partition in north classroom installed – staff received training on use and care.
- Dance Studio hardwood floor installation continued.
- Carpet installation proceeded in offices, classrooms, and main hallway.
- District staff received training on the commercial kitchen equipment.
- **GRAND OPENING is Saturday January 5th, 2013 from 1-4pm.** Come tour the beautiful building and enjoy class demonstrations, live music, boutique sale, raffles and goodies!

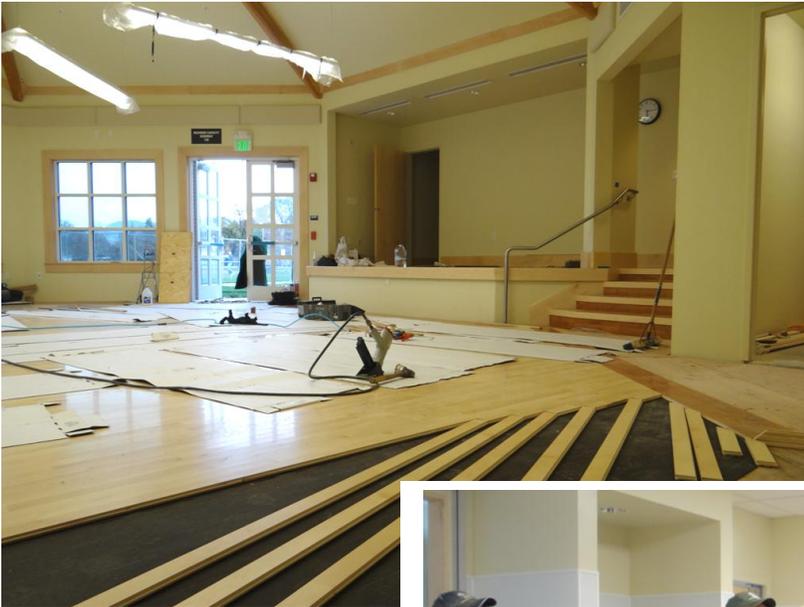

Left: Dance Studio hardwood install in progress.

(20121203-1656)

Below: Staff training on the commercial convection ovens in the large kitchen.

(20121204-1045)



Applying another top coat on the Chateau Room floor in preparation for vinyl floor covering installation.

(10121204-1147)



Ellis & Ellis crew installing one of several way-finding signs around the project sites in Pleasant Hill Park. The signs were designed by GNU Group. (20121204-1124)



Senior Center front entrance wells for donor pavers to be installed soon by District staff. Another way-finding sign for the site. (10121204-1626)

Teen Center

- Interior building signage installation proceeded.
- Monument sign base was poured – sign installation planned in this upcoming week.
- Punch-list repairs are nearly complete.
- The TEEN CENTER is open after school Monday through Friday 2:00 – 6:00pm for grades 6-12. Come on in!
- Teen Center spaces are available for rentals – see our website for details.



Teens enjoying the Wii action after school at the Teen Center. (20121203-1612)

Community Center

- Under-slab plumbing and electrical work continued.
- Forms construction for planters and stem walls continued.



Under-slab work progressed as possible this week – the site appears to drain fairly well. (20121207-1727)
