

Bond Projects Updates for Monday 13 May 2013

Community Center

- Mechanical, electrical, and plumbing installation continued.
- Roof framing and sheathing nearly complete.



(20130510-1358)



Looking into a preschool entryway – ducting, fire sprinklers, domestic water pipes, and electrical conduits are all being installed.

(20130510-1359)


Approaching the front entry from the east corner of the WeeTot Room. (20130507-1403)





Overlooking the WeeTot Room and the Workshop.
(20130510-1407)

Overlooking the classroom & offices roof toward the playground below.
(20130510-1407)

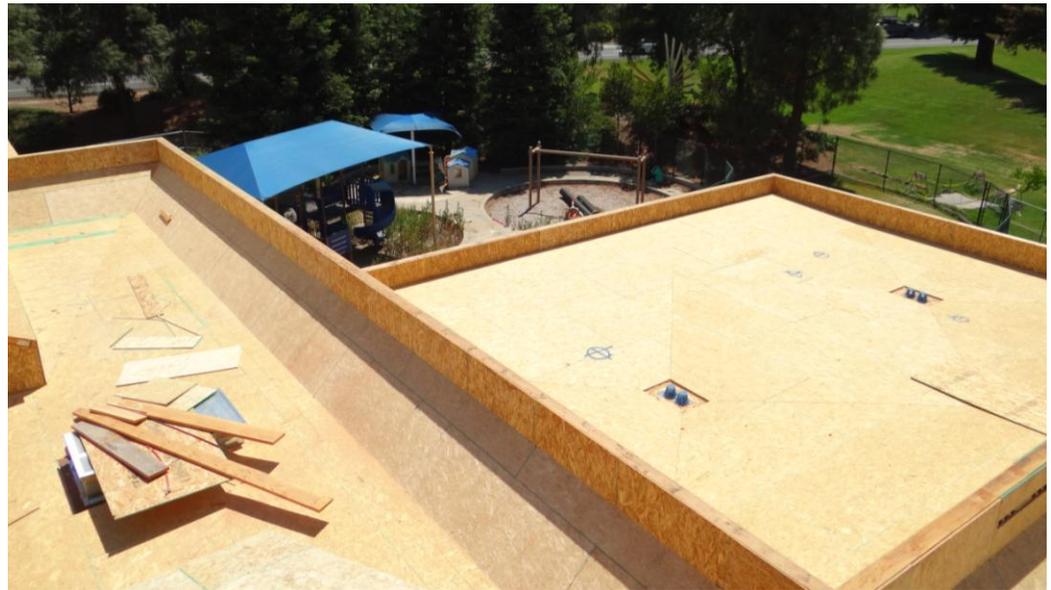

Looking south along the classrooms roof. Peak of overhang of the Dance Studio roof on the left. (20130510-1410)

Platforms for a pair of 1500 lb heat pumps have been added to this mechanical area on the roof. (20130510-1415)



View from an attic space down into the main hallway and into two classrooms. The operable wall will be stowed in this structure when it is open.

(20130510-1426)

A set of classroom window frames have been installed as a mockup for approval of the inspector, before the rest of the frames can be installed. This is the finished color of the frames. (20130510-1438)





View west from the attic toward the preschool rooms. The McHale Room and main entry are on the left. (20130510-1430)

Another look into the Preschool Rooms. (20130510-1444)



HVAC ducting and pipes have been installed in the Dance Studio and Perera Pavilion ceilings. (20130510-1439)

Pleasant Oaks Park

- The District Board awarded the Pleasant Oaks Park Project to Goodland Landscaping Construction at their regular meeting 5/9/2013.
- The Groundbreaking for the project will be at the park 5/30/2013 at 4:00pm at the existing playground.
