

Bond Projects Updates for Monday 15 October 2012

Senior Center

- Flooring installed on platform areas.
- General site cleanup continued.
- Audio-Visual package installation began.



South face – front – of the new Senior Center (20121009-1549)



Pre-finished hardwood flooring on the Multi-Purpose Room platform.

(20121012-1701)

Multi-Purpose Room:
The coffee service area
between doors to the
hallway adjoining the
kitchen. Open door
looking east into the
park.

(20121012-1701)



Teen Center

- **MILESTONE – Substantial Completion achieved as of Tuesday 10/9/2012 8:00am**
- Punch list items work and final inspections are still in progress.
- Audio-Visual system equipment installation continued.
- Standard furniture package delivery and installation completed. Final furniture package delivery and installation is scheduled for Wednesday 10/17.
- **The Grand Opening is scheduled for Saturday October 20th – see our website for details!**



Looking NNW from the roof – the new gated access to the Aquatics Center, ball fields in the park, and courtyard storage for the new Teen Center program equipment.

(20121008-1645)


Walking the roof to check off punch list tasks for Substantial Completion. Round elements are exhaust fans for the new park restrooms.

(20121008-1649)



West exposure clerestory windows have tinted glass and motorized shades to help control the interior temperature.

(20121008-1648)

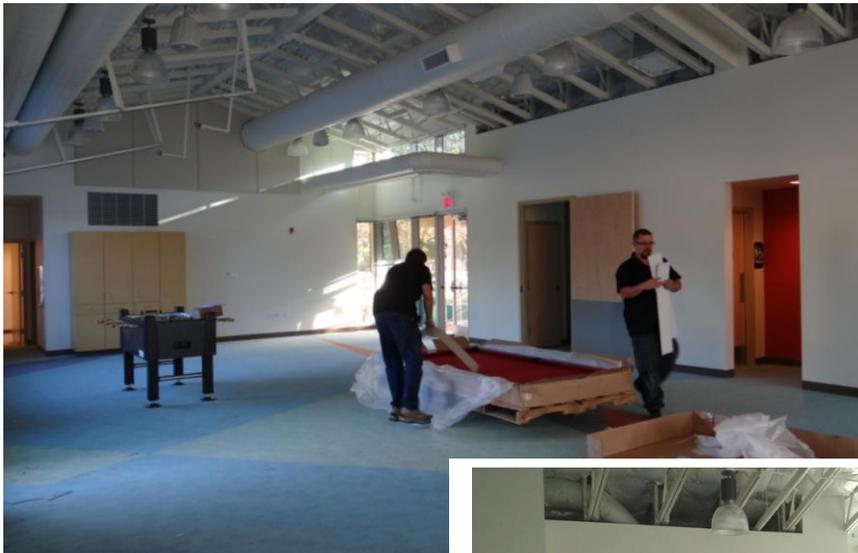

Installers unpacking the new pool table.
(20121009-0844)

Occasional tables and some comfortable seating arrived with this package. More furniture to come in the new week.
(20121009-0844)



Community Center

- Building layout and underground utilities work continued. Photo below: rebar on site. (20122011-1010)
- Expected concrete pour for footings: week of October 22nd



Pleasant Oaks Park

- City Planning Commission continued discussion of the project to Tuesday October 23rd at 7:30pm
