

## Bond Projects Updates for Monday 16 April 2012

### Senior Center

- A rainy week except Monday 4/9
- Made progress on framing & blocking
- Made progress on roof trusses, plywood sheathing, & fascia on Dance Studio
- Continued waterproof flashing membrane installation on the window openings
- Installed the metal roof framing elements for the trash enclosure



Waterproof membrane visible around window openings. Trash enclosure roof far right. (20120413-1523)



Left: Exterior view - Plywood layer and fascia (trim board) on Dance Studio, including dormer.

(20120413-1533)

Right: Interior view – Dance Studio becoming enclosed as the roof materials continue to be installed. View up into dormer space.

(20120413-1534)




Teen Center

- Stucco scratch coat completed & inspected, then 2<sup>nd</sup> layer (called the brown coat) was applied.



Left: West wall of Meeting Room  
(20120411-1137)

Below: View from the northeast corner.  
(20120411-1142)

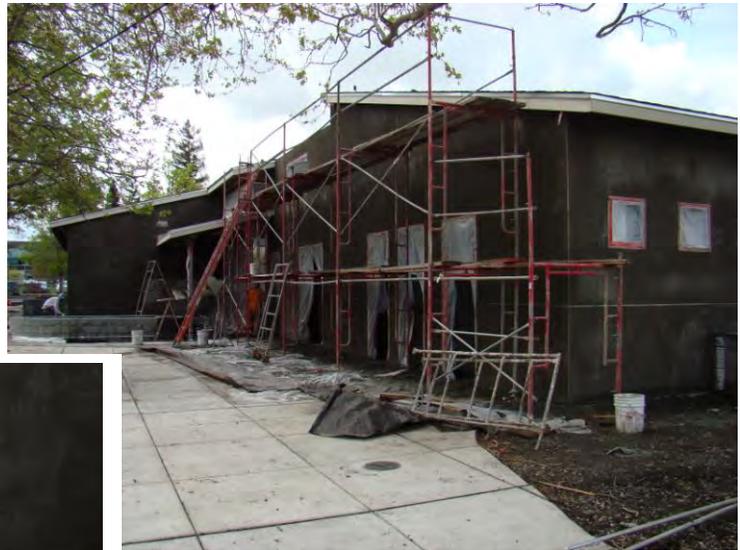

Above: Worker leveling out the brown coat on the east side of the building.  
(20120411-1144)

Right: Looking into the Park Maintenance shop, northwest corner of building.  
(20120411-1143)



Community Center

- Mandatory pre-bid conference was held at the Public Services Center Friday 4/13. Twenty-eight general contractors attended.
- On Tuesday 4/12/2012 the City Planning Commission approved the District's exterior signage design and locations.
