

Bond Projects Updates for Monday 17 December 2012

Senior Center


- Floor coverings and baseboard trims installation continued.
- Punch list tasks continued.
- Offices: furniture package was delivered and installed.
- Draperies were installed in the Library/Lounge.
- Audio-visual components were installed in the Chateau Room.
- Network switching equipment was installed and configuration begun.
- Monument signs at Gregory Lane entrances to Pleasant Hill Park and to the Senior Center were installed.
- Work began installing donor paver in main walkway – performed by District staff.
- **GRAND OPENING is Saturday January 5th, 2013 from 1-4pm.** Come tour the beautiful building and enjoy class demonstrations, live music, boutique sale, raffles and goodies!



Main entry hallway carpet with inset center.

The display cases have all their glass and lighting installed now.

(20121210-1621)

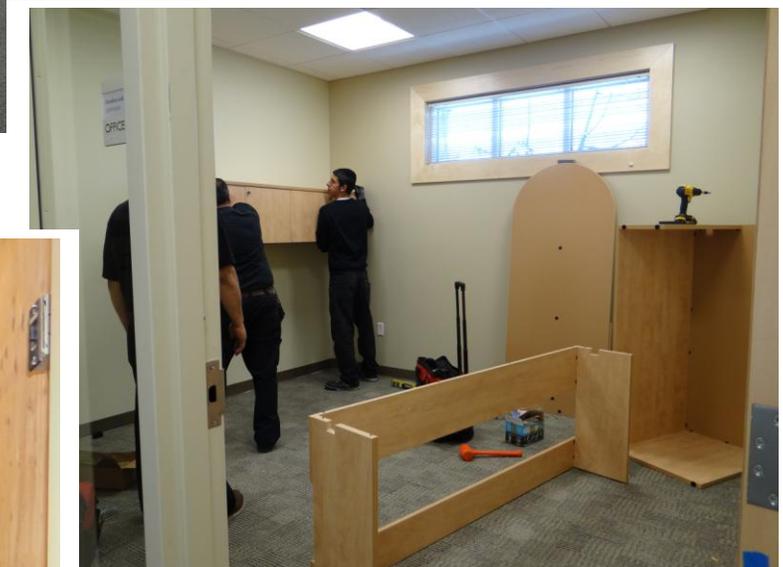

Above: OneWorkPlace crew installing the Steelcase office sets. (20121213-1309)

Left: District contractor "JD" of Ontai assembles a switch for rack-mounting. (20121213-1613)



Spinitar crew installing and testing one of the digital projectors suspended from the Chateau Room ceiling.


(20121210-1624)



Ellis & Ellis crew assembling the new Senior Center monument sign at the Gregory Lane entrance.

The GNU Group designed all signage for the new facilities.

(20121211-1017 & 1124)

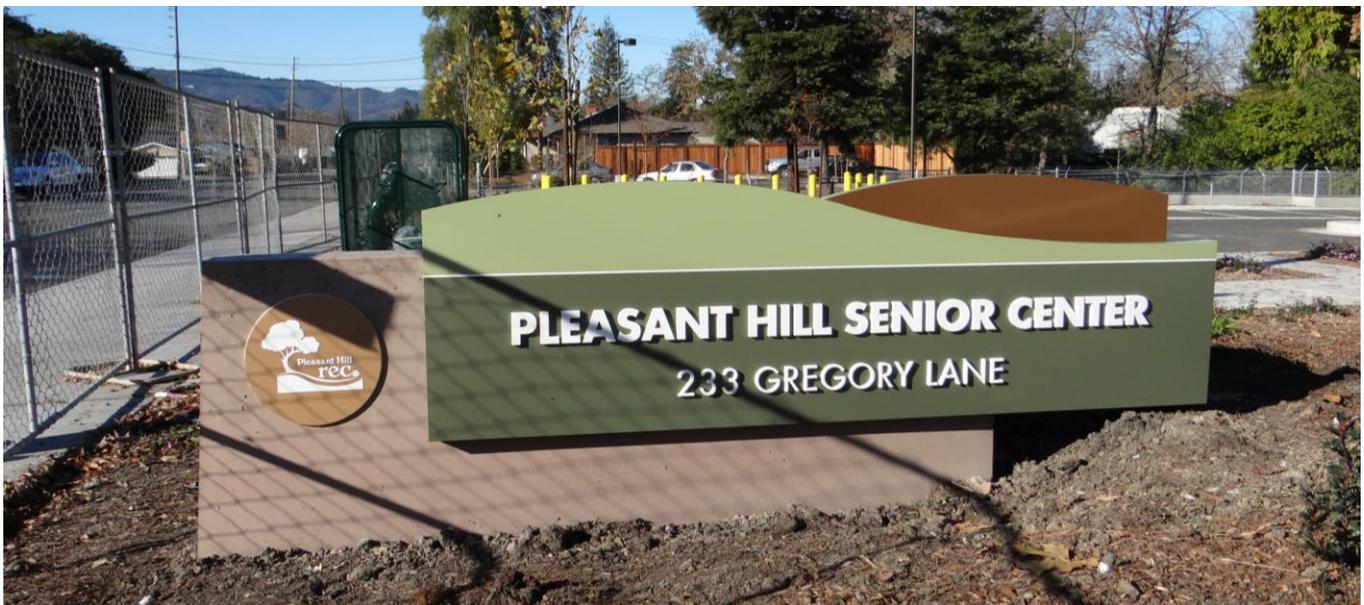



Ellis & Ellis crew installing the solid aluminum lettering on the front of the new Senior Center.

(20121211-1144)

From a main entry door to the room: A partial view of the newly installed vinyl floor covering in the Chateau Room.

(20121213-1514)



Senior Center Supervisor Kendra Luke checking out the ongoing installation of donor pavers by Craftsman Todd Smith in the parking lot walkway.

(20121213-1213)

Community Center:

- Concrete was poured for the stem-walls and building-integral filter planters.
- Under-slab plumbing and electrical work continued.



Pouring the stem walls and portions of the filter planters - another job for the long arm of the concrete pump.

(20121210-1324)

Filling the forms at the northwest corner of the building – the future preschool program rooms of the new Community Center.

(20121210-1337)



Looking west into the future kitchen service hall and restrooms area, evidenced by the wrapped plumbing stub-ups.

(20121210-1325)
