


Bond Projects Updates for Monday 18 June 2012

Senior Center

- Insulation and sheetrock installers continued their work.
- Electrical, mechanical, and plumbing infrastructure work continued.
- Roof felt membrane was installed on octagonal rooms.



Looking northeast from inside the Library /Lounge (20120613-1054)

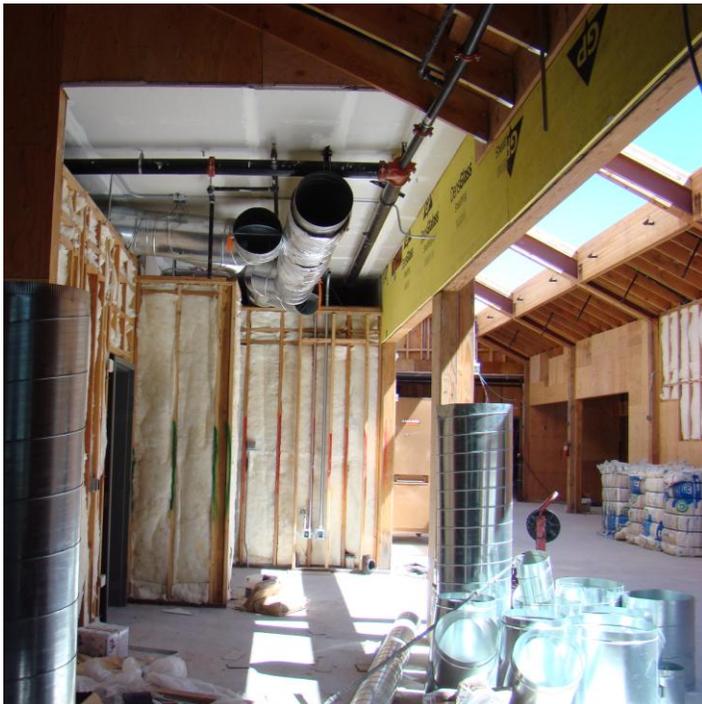

The building infrastructure goes up layer by layer. Looking north from the Library/Lounge entrance.

(20120613-1055)



CC Café looking north into the restroom and chef's office areas. Plumbing, electrical, and data infrastructure visible in the framing.

(20120613-1058)

CC Café ceiling infrastructure additions – the data cable pathways have been installed (see top of photo)

(20120613-1104)



Applying rolls of felt to the octagonal roofs

(20120614-1517)

Teen Center

- Some work was accomplished on sheetrock taping and electrical infrastructure.
- Picnic Area: Gravel was spread over the landscape fabric and irrigation installation began.



Looking north in the main room
(20120612-1344)



Above & left; the picnic area irrigation and gravel
(20120613-1122&1123)

Community Center

- The **Community Center re-bid** is coming up, with a **PRE-BID Conference on Friday 6/22/2012 at 10a.m. at the Public Services Center, 310 Civic Drive, Pleasant Hill CA 94523**
