

## Bond Projects Updates for Monday 19 August 2013

### Community Center

- Concrete pours: front and east feature wall footings, filter planter bottoms.
- **MILESTONE:** Brown-coat (second layer) stucco applied.
- Electrical: wire pulling continued throughout the building.
- Sheetrock installation continued (working west to east in the building).
- Glazing installation continued.



Glazing is being installed in the interior storefronts. View into the dividable classroom space.

(20130813-0826)

View from one preschool room through double doorways into the next preschool room.

(20130813-0848)




Workers applying the brown coat on the south wall of the facility offices. This layer will cure for 28 days before the finish coat is added.

(20130813-0834)





Glazing on the east end of the Perera Pavilion reflects the beautiful park setting. (20130815-1524)

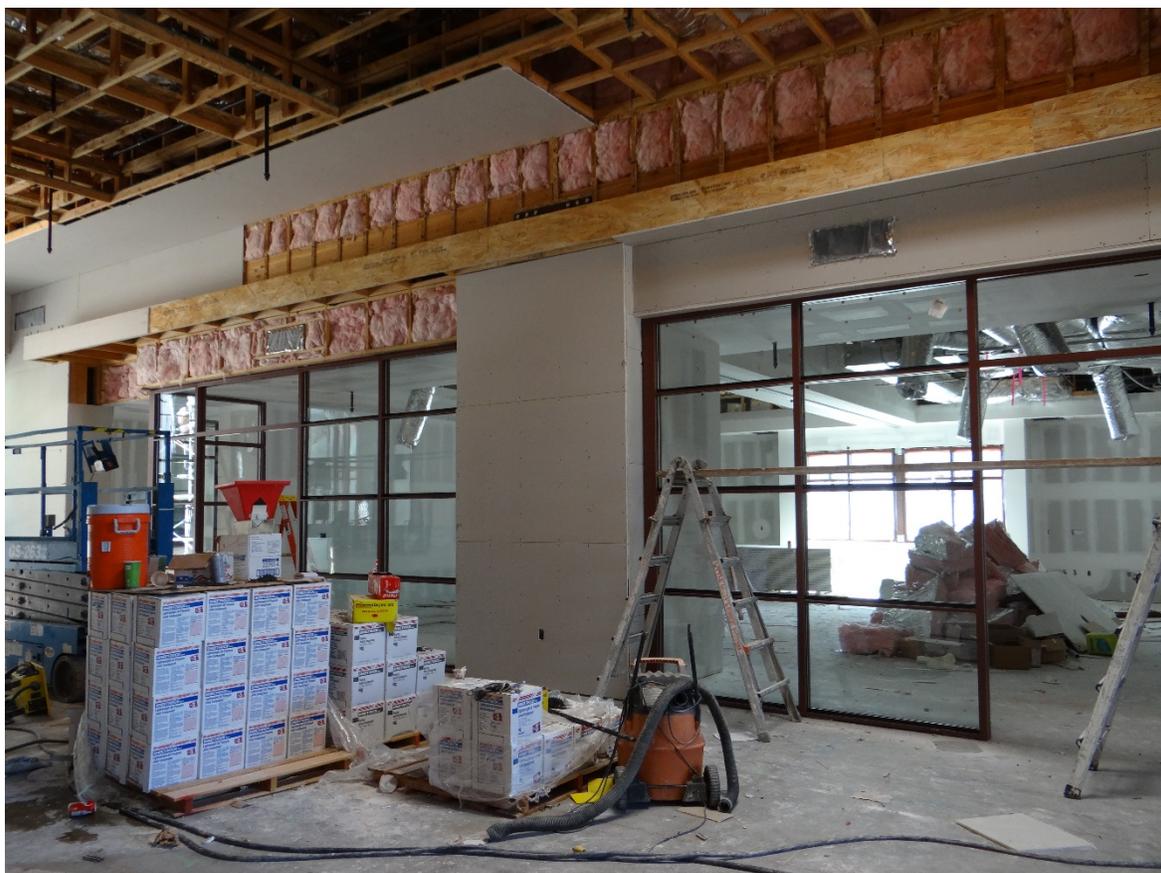

Sheetrock is going up in the main hallway. (20130815-1529)



Above: The preschool walls are ready for their sealer coat. (20130815-1533)



Left: The feature wall footing was poured this week. The top of the wall will follow a gentle arc, so the vertical rebar will be cut accordingly.

(20130816-0953)

Workers installing sheetrock in one of the main hallway skylight bays.

(20130816-1000)



Pleasant Oaks Park

- Curb and gutter formed and poured for the Monticello parking lot.
- Base rock compacted for the baseball fields.
- Storm drain tie in accomplished at the corner of Santa Barbara and Monticello.



The retaining wall for the parking lot has been completed.  
(20130815-1425)



Curb and gutter forms in the Monticello parking lot.  
(20130815-1425)



An example of the acres of ball fields compaction.  
(20130815-1426)



Trenching across a ball field for high speed rotor irrigation.  
(20130815-1428)
