


Bond Projects Updates for Monday 25 June 2012

Senior Center

- Security Systems and Signage are out to bid for both the Senior and Teen Centers.
- **MILESTONE** – Fire sprinkler system charged - passed inspection & testing.
- Roofing felt layer work continued.
- Paper and lathe finishing up on exterior walls.
- Insulation and sheetrock progressed to the south end of the interior.
- Mechanical, electrical, and plumbing installations continued.

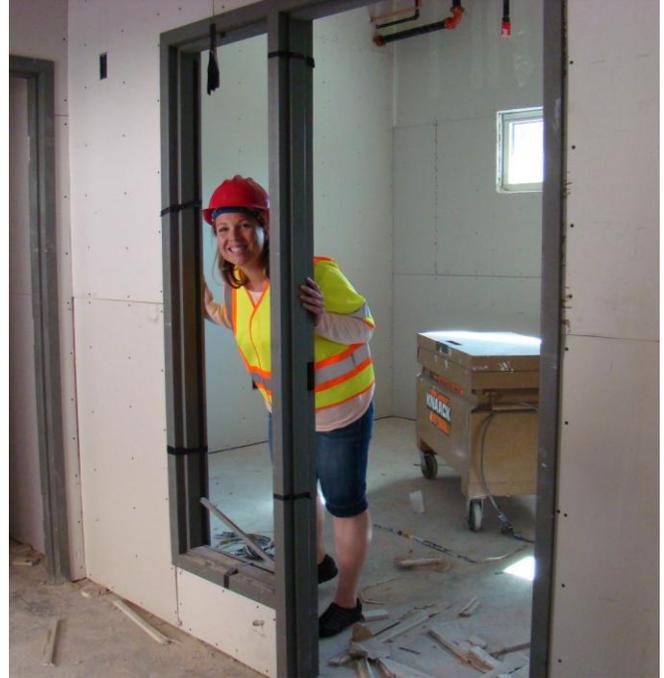

Kendra visiting her new office (20120622-1703)

Left: Office hallway, looking north (20120619-1002)



Roofing progress by Wednesday

(20120620-1138)



Entry hall with plastic over the skylight bays for temporary weather-tightness. Insulation & sheetrock going up, while electricians pull wire through the conduits.

(20120622-1251)

More data pathway and electrical infrastructure installed in the Multi-Purpose Room roof framing.

(20120622-1253)



Dance Studio insulation and sheetrock progress. HVAC ductwork stationed on the floor in readiness for installation.

(20120622-1257)



CC Café – the ladder is in the kitchen, seen through the upcoming lunch service window.

(20120622-1629)

Looking southeast in the Library/Lounge – Kendra is checking out the new fireplace, sitting on its platform next to the media storage unit.

(20120622-1630)



Looking southwest in the Library/Lounge – Kendra inspects the media storage area.

When the Center is open, people will be able to borrow movies from this cupboard by checking them out with an attendant.

(20120622-1629)

Teen Center

- The last of the cedar siding was installed on the upper front side of the building.
- More of the south side “whacky mullions” were fitted.
- Irrigation infrastructure was completed for the new picnic area.

Installing another section of the “Whacky Mullions” – the curtain wall feature of the new Teen Center.

(20120622-1304)



The last sections of cedar siding were installed on the upper south & southeast faces.

(20120622-1307)

Community Center

- The CATV bypass for continuous service to PHPD was completed this week.
- The **Community Center was put back out to bid this week.** The pre-bid conference on Friday June 22, 2012 had a good turn-out of general contractors.
- **Bid Opening is scheduled for July 17, 2012 at 2:00pm** at the District Office, 147 Gregory Lane, Pleasant Hill 94523.



CATV bypass trench (20120621-0834)
