

## Bond Projects Updates for Monday 26 March 2012

### Senior Center

- Begin install trusses between Dance Studio roof glulam beams
- Install all 8 CC Café roof glulam beams
- Begin install glulam roof beams over large Multi-Purpose Room
- Irrigation, electrical, and Bocce Courts flatwork forms & rebar all in progress



Dance Studio glulam beams without the temporary center support column.

20120319-1635

Dance Studio looking NNW

20120319-1636



Dance Studio roof beams now getting additional trusses

20120323-1438



Bocce Courts with forms, rebar, light pole bases and center benches installed. Looking NNW at new Senior Center.

20120322-1506



Main beams are up over the CC Café – compare with architect’s rendering below. (20120323-1433)



First two large glulams were attached to the large steel truss over the Multi-Purpose Room .

20120323-1441


Teen Center

- Paper and lath work continued in preparation for stucco application
- Composition shingle roofing installation proceeded through the week
- Glass panel “garage” door installed between the Game Room and the Courtyard
- Park maintenance roll up door installed
- Irrigation system work continued



Exterior view of the “garage” door that will open the Teen Center to the Courtyard. The space can also be opened to the pool deck by wide gates on the opposite side of the Courtyard.

20120320-1330

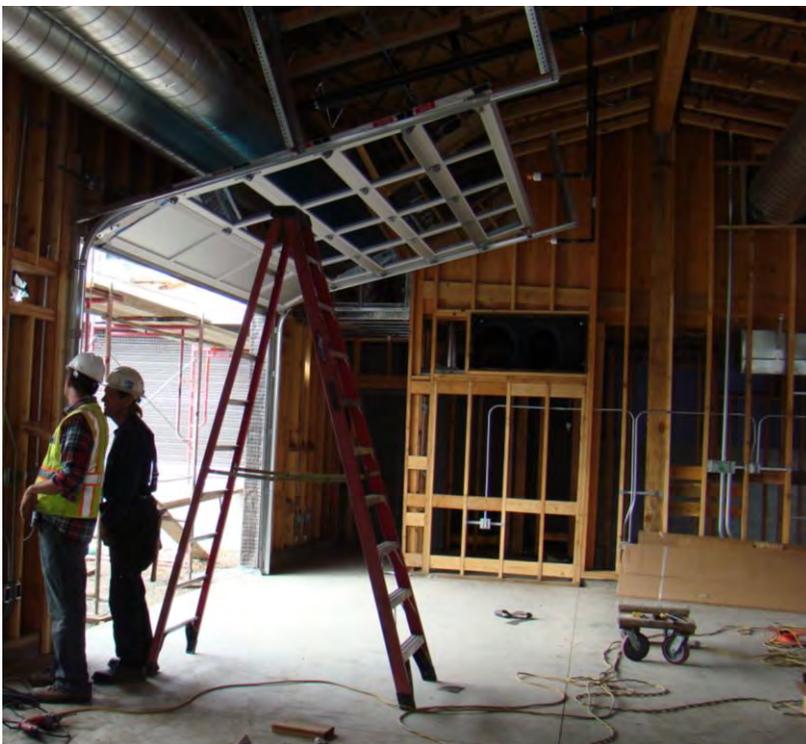

The glass paneled “garage” door:  
Above – closed position

Left -- in the open position over  
the Game Room area.

20120320-1355 & 20120320-1628



Architectural grade composite singles being installed. ( 20120322-1537)



The masonry portion of the building is also papered and wire-lath covered before it is stucco coated.

This is the north end of the structure – Park Maintenance work area and restroom windows visible.

20120323-1526

### Community Center

- Permitting, easements, and constructability review/response in process.
