

Bond Projects Updates for Monday 5 August 2013

Community Center

- Insulation and sheetrock installation continued.
- Standing-seam metal roofing mockup installed in place – pending factory service rep acceptance.



View looking west at the new Community Center from the park. (20130730-0904)

The partially insulated wall in the main hallway is the future home of glass art pieces.

(20130730-0915)



View into the large events area through the Dance Studio and Perera Pavilion – from the main hallway.

(20130730-0919)

The Dance Studio ceiling is lower than the Perera Pavilion ceiling. The rooms can be partitioned from one another by operable walls.

(20130730-0921)




The north wall in the Dance Studio will be covered with mirrors.

(201307-0922)

Workers installing sheetrock overhead in the WeeTot Room entryway.

(20130730-0925)

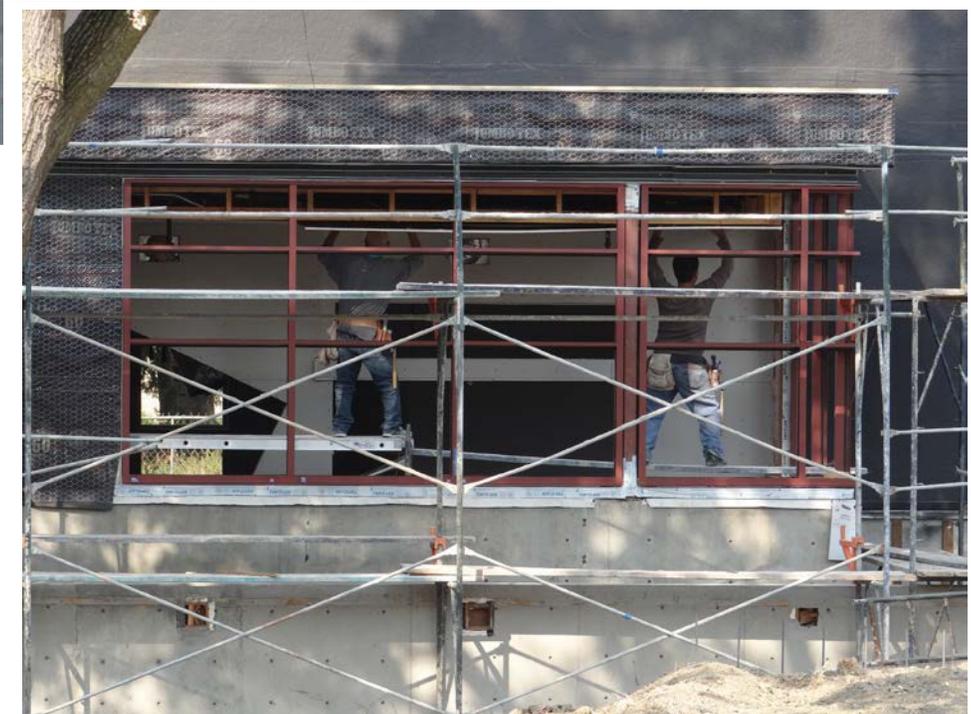

View south of the main events entry. Storefront frames are nearly completed and glazing is scheduled to begin within two weeks.

(20130730-0925)



Crew in the distance is installing the standing seam metal roof mockup.

(20130730-1637)

A group of air handling units and two heat pumps. HVAC equipment is installed on several locations on the roof.

(20130730-1630)



Likely the last look at the large steel beam across the front of the building. The soffit will be closed up in the near future, and this area only accessed for infrastructure testing and maintenance.

(201307-1646)

Pleasant Oaks Park

- Parking lot on Monticello was cut to final grade.
- Concrete footings were poured for the new backstops.
- Grading of future playing fields continued.



Above left: grade cut for parking on Monticello side. Compaction has been met for the parking area.

Above right & right: footings poured around new backstop posts.

(POP photos and info by Amanda)



Infrastructure excavations continued at several locations on the site. (20130801-1010)
