

# Bond Projects Updates for Monday 7 May 2012

## Senior Center

- HVAC units all lifted to the roof & last large beam lifted and set in place over the Multi-Purpose Room
- Continued installation of window “awnings”
- Continued roof framing and sheathing
- Parking lot irrigation systems worked on all week long
- Concrete picnic table shipment received – 2 for Bocce Courts



Lifting the HVAC units onto the roof


(photo: Gordon Johnson 20120430-1041)



Fitting the last large beam into the octagon – lifted by crane  
(20120430-1159)



## East Elevation: Multi-Purpose Room (20120501-1140) Dance Studio Class/Meeting Room

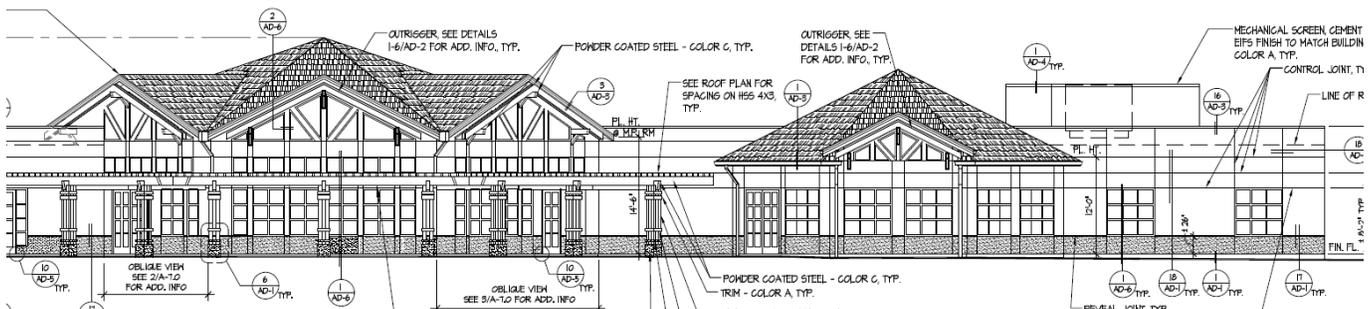

Looking west over the Multi-Purpose Room roof framing  
(20120502-1328)



With all 8 beams now in place, progress on framing the large octagonal roof moves quickly  
(20120502-1324 & 1328)



Library/Lounge Platform and framing for gas fireplace and video/book storage  
(20120504-1226)

Teen Center

- HVAC unit lifted by crane to the flat area of the roof
- Work began on installation of hand railings at both ramp areas of the facility



Lifting the HVAC unit to the mechanical area of the new Teen Center roof  
(Photo: Kat Hunn 20120430-1335)



Hand railings along the exit ramp from the northeast corner of the pool deck  
(20120504-1220)

Community Center

- Bid Process: Addenda #'s 1-3 are in progress for imminent release to contractors holding the bid set
- Permitting agencies continue to review updated materials as they become available
- Public Bid Opening is currently scheduled for May 15<sup>th</sup> at 2pm at the Admin Office at 147 Gregory Lane
