

Bond Projects Updates for Monday 23 September 2013

Community Center

- Site work continued on all sides of the building.
- Forms installed for tiered patio adjoining the bench seat around the Hackberry.
- Trash enclosure foundation: footings excavated and rebar work began.
- Electrical: installing wiring in conduit runs throughout interior.
- Main switch gear installed and passed inspection.
- Sheetrock installation, taping, and sealing continued.
- Construction of bioswales continued.

View east along the events rooms – rebar for patio and walkway installation continues.

(20130916-1450)




Looking east – forms were constructed for the stepped west end of the patio. The steps adjoin the “Republic Room” (classroom) exterior wall.

(20130916-1451)

A District Park Maintenance crew began removal of existing playground fiber and sand, in order to repair the drainage and refresh the play area materials.

(20130919-0807)



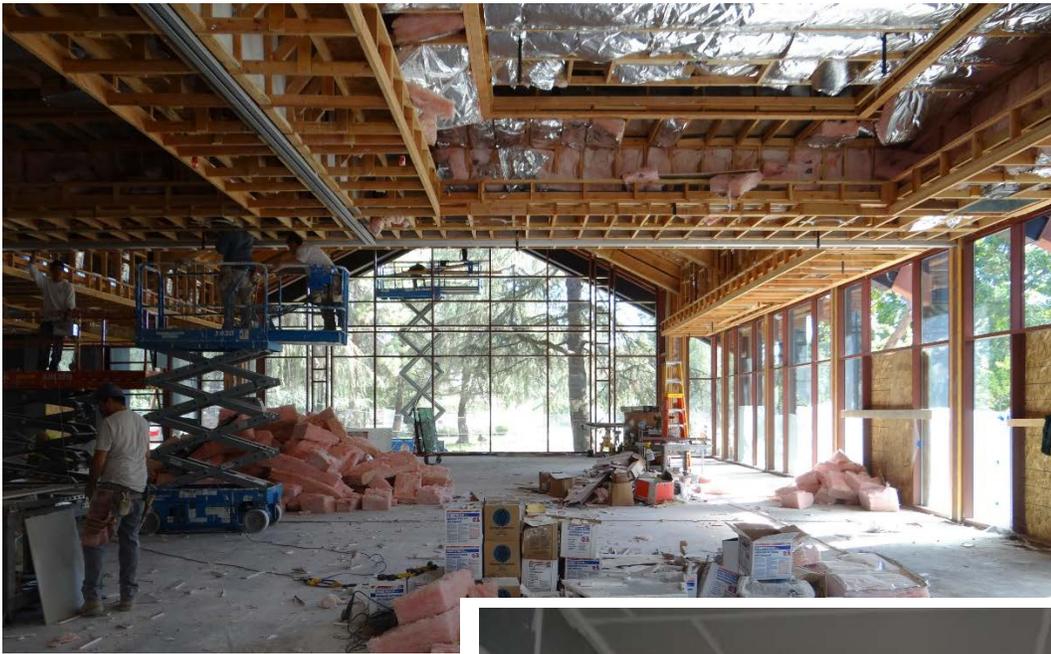

Electrical and telecommunications wiring is being pulled throughout the facility. Sheetrock work also continues.
(20130920-1031)

A view from the front entry through to the “back door” of the main lobby.
(20130920-1028)



An example of a tubular skylight installed in the connecting hallway between the programs area of the building and the events area. The restrooms are also in this hallway.
(20130920-1030)



T-bar track for suspended ceiling tile has been installed in the preschool rooms. Data cabling can be seen staged on the left. (20130920-1036)

The main feature wall forms at the front of the building are nearly ready for a concrete pour. (20130920-1039)



The new drivable turnaround is coming into shape. (20130920-1042)

Pleasant Oaks Park

- Hawthorne Drive is now closed for the duration of asphalt paving to the new curb and gutter.
- Backstop and dug-out structures construction continued.
- Concrete entrance driveways were poured on Monticello side parking lot.
