

Bond Projects Updates for Monday 6 January 2014

Community Center

- Landscaping activities by the District Park Maintenance crew proceeded.
- Telecom, electrical, lighting and plumbing installations continued.
- Trim work on interior and exterior features continued.
- Operable partitions assembly finished and furniture installation began.
- GRAND OPENING is scheduled for January 26th – see our website for details!

Preschool Rooms are getting their finish plumbing. Sinks will be installed in the low counters for the kids' hand-washing.

(20140102-1600)



Ceiling tiles installation will be completed when various inspections of the infrastructure have concluded.

(20140102-1600)


Tables and chairs are staged for placement in the classrooms/meeting rooms.

(20140103-1524)



In the main entry lobby
the east wall surfaces
are awaiting vinyl
coverings.

(20140102-1603)

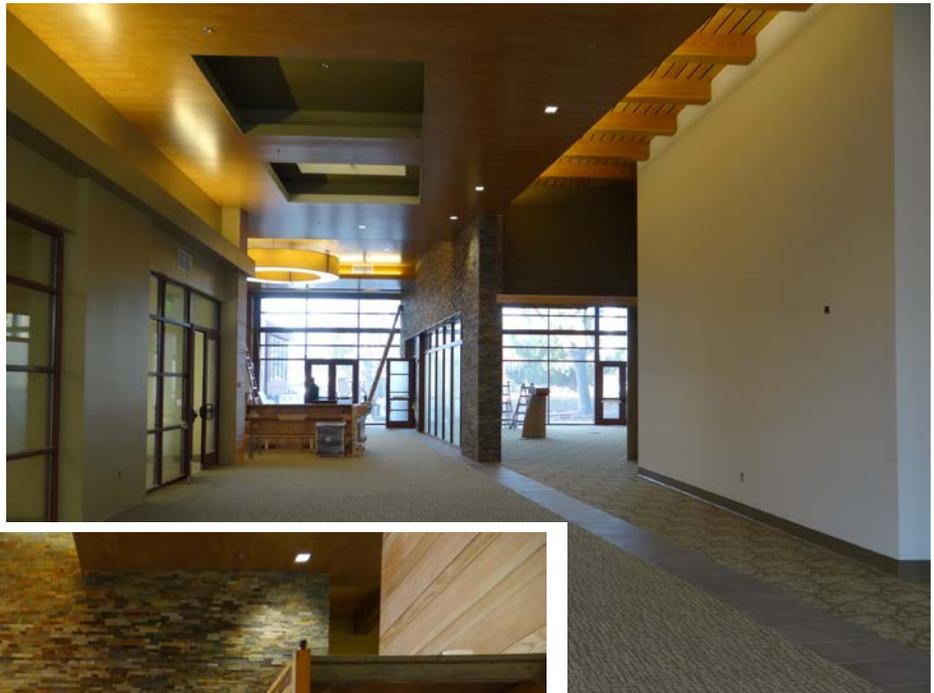

The main lobby
reception counter is
being assembled.

(20140103-1038)

A fleet of new banquet
chairs is staged in the
Perera Pavilion.

Banquet tables and
other furniture arrive in
the new week.


(20140103-1032)





Operable wall panels are being hinged together in pairs as part of their finish assembly.

(20140103-1032)

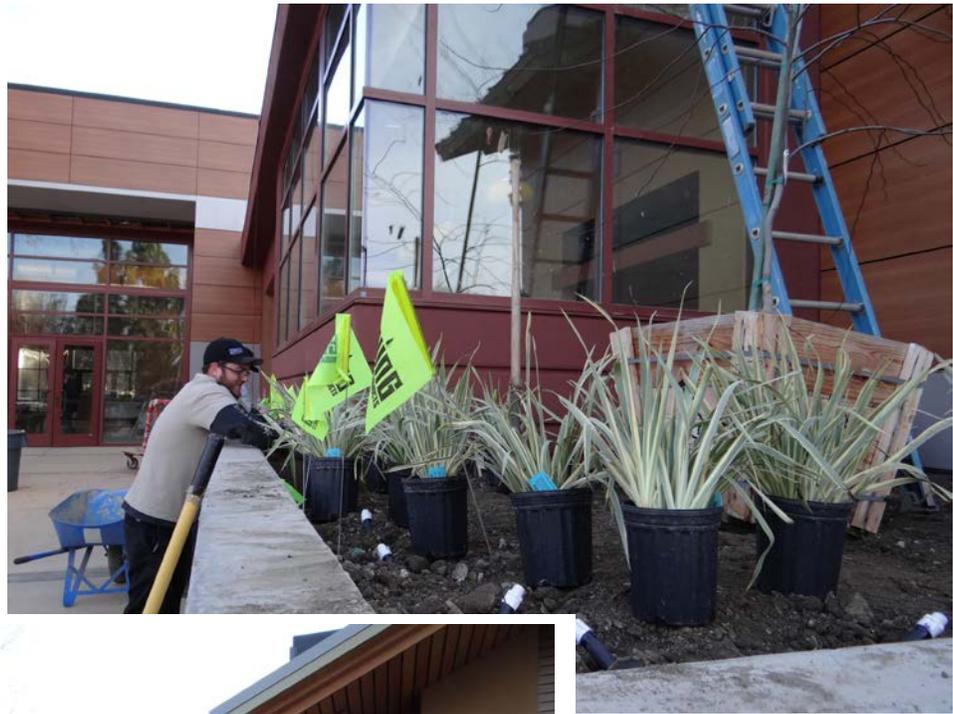

Above and left: Park Maintenance working on irrigation and planting around the site.

(20140102-1604 & 1609)
