

Bond Projects Updates for Monday 13 January 2014


Community Center

- Furniture delivery and installation completed.
- Various interior and exterior trims & finishes (including vinyl wall coverings) continued.
- Final concrete pours accomplished.
- Construction trailers pulled off laydown area and asphalt repair began.
- Trespa panels installation continued.
- Network head end equipment install and configuration proceeded.
- Lighting, electrical, and plumbing finishes continued.
- Cabinetry installation continued.
- Landscaping installation continued.
- Mirrors installed on Dance Studio walls.
- Interior wood doors and hardware installation continued.
- GRAND OPENING planned for Sunday January 26th – see website for details!



Banquet tables
being delivered to
the Perera Pavilion.


(20140106-1008)

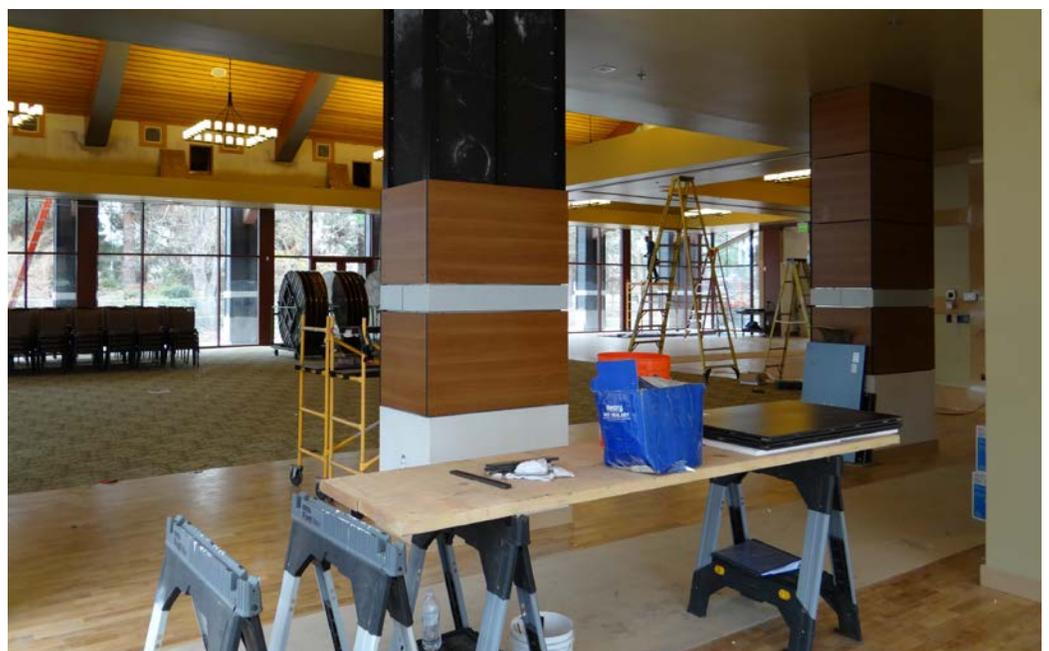

Trespa panels
being installed on
the interior
columns.

(20140108-1137)

Mirrors installed in the Dance Studio are useful for ballet classes as well as bringing reflected light into the room.
(20140108-1203)

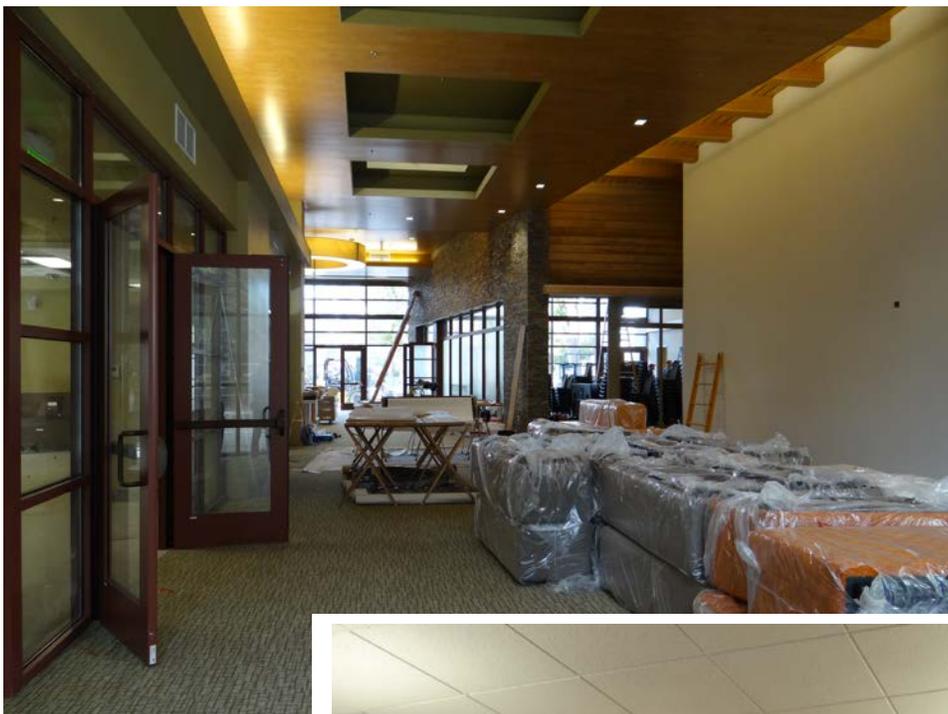

“Jumble” seating will be unwrapped after the carpenters finish their trim-work in the main lobby.
(20140108-1556)

Drop ceiling tiles install is nearly complete in the Preschool Rooms.
(20130110-1641)






Above: Roll-down sun shades are installed on the south exposure of the events rooms. Dance Studio entry doors install in progress. (20140109-1956)



Above: The events entry trellis is being painted before the glass rain cover panels are dropped in. (20140110-1559)


Left; Concrete pour in the trash enclosure. (20140109-0954)



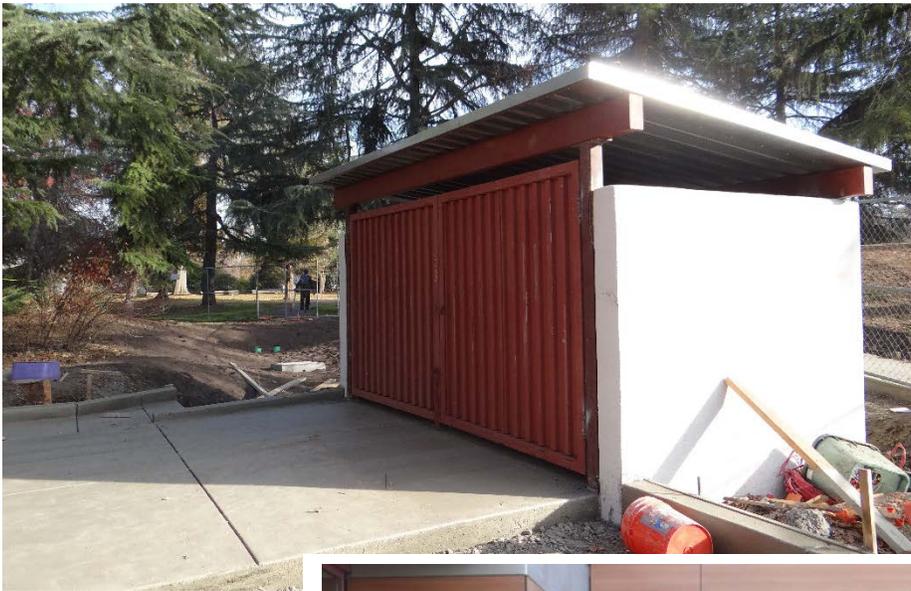

Trash enclosure sporting its new gates and roof.
(2014-0110-1601)

Welders assembling the steel pan for the front entry bench. It was later filled with concrete – awaiting its tile top-finish.
(2014010801653)

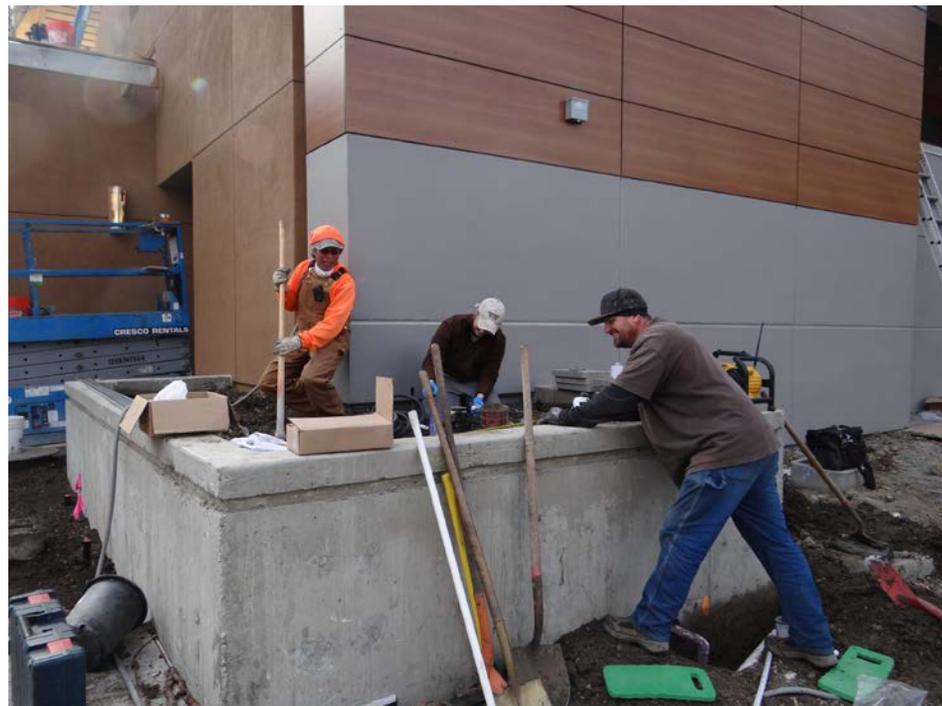

District Park Maintenance staff prepping and planting a filter planter that treats roof run-off.
(20140108-1207)
