

Bond Projects Updates for Monday 20 January 2014

Community Center

- “All hands on deck” – electrical, mechanical, plumbing, painting, glazing, wall & floor coverings, AV, cabinetry, door hardware, kitchen equipment, drop-ceilings, landscaping, art installation, signage, data infrastructure, and more.
- Ongoing inspections by various permitting agencies.
- **GRAND OPENING scheduled for Sunday January 26th – see website for details!**



Trims and wall coverings work tables are set up in the main lobby.

(20140113-0942)


The major donor display signage is being installed in the main lobby.

(20140117-1504)



An ice maker being installed in the catering kitchen. Plumbing and electrical connections were made to all the appliances.

(20140114-1619)

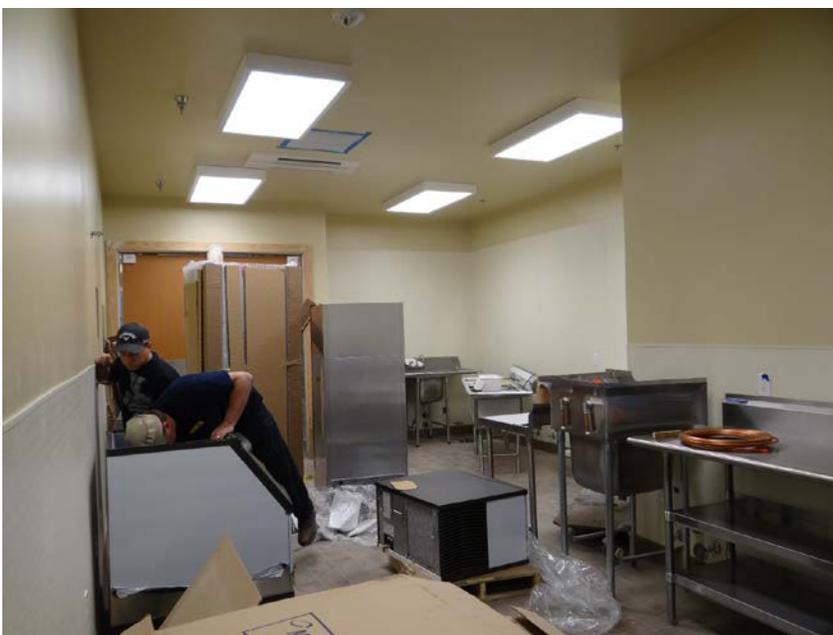

“Jumble” seating still in its protective wrapping, waiting for the carpentry dust to settle and be cleaned up.

Scaffold is for the wall-covering installers’ use.

(20140114-1535)



Vinyl wall covering going up on the east wall in the main lobby.

(20140114-1620)

East wall in the McHale Room: acoustic paneling and custom framed art pieces being installed.

(20140117-1505)





Above: reception area art installed. (20140117-1321)
Left: Acoustic panels and finishes being installed in the Perera Pavilion. (20140116-1009)

Preschool Room #1 is nearly ready for final cleaning.
(20140116-0944)






Looking east: the darker sod in the foreground covers the bioswale and is “no-mow” grass. The more familiar park-mix sod is installed everywhere else.
(20140116-0933)

Pleasant Oaks Park

- Monument signs were installed last week at the corners of Santa Barbara & Monticello and at west corner on Hawthorne.
- **GRAND OPENING scheduled for Sunday March 2nd – see our website for details!**

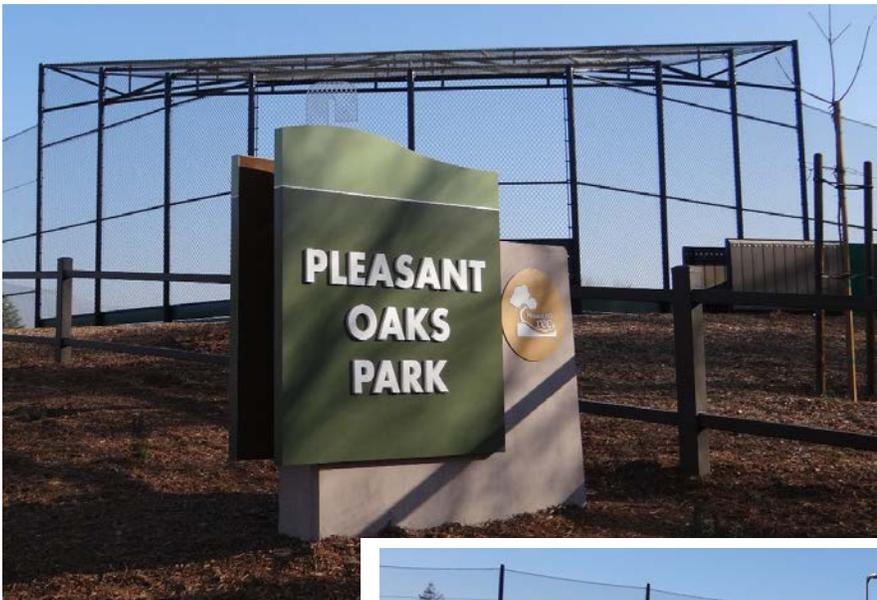

Left: the monument sign on the west end of Hawthorne.
(20140117-1604)
Below: the monument sign at the corner of Monticello and Santa Barbara. (20140117-1559)

