

Bond Projects Updates for Monday 25 November 2013

Community Center

- Installation of Trespa panels continued.
- Site work continued, with rain interruptions.
- Hardwood flooring installation began in the events lobby.
- Lighting installation continued.
- Installation of Audio-Visual equipment continued.
- Interior trim work continued.



Left: Trespa panels installation progress on the east wall of the WeeTot Room.

(20131121-1356)


Below: View east from the Preschool entry door – craftsmen installing Trespa panels on the upper north face of the building.

(20131122-0944)




Installer spreading adhesive for the hardwood flooring in the events area.
(20131121-1431)

Below: view from hallway to the east (side) doors of the events lobby. Hardwood flooring installation in progress.
(20131122-1412)

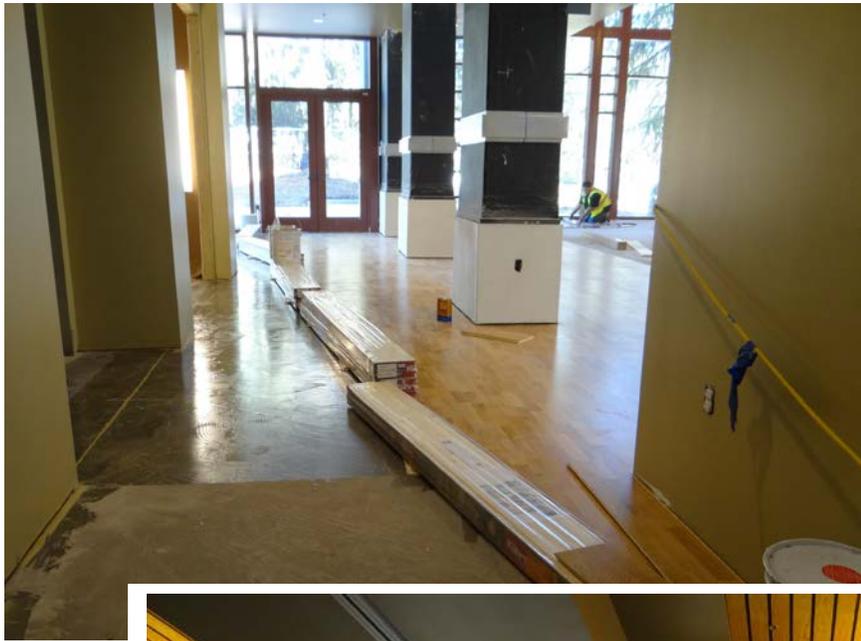


The Dance Studio slab levelling compound is drying for the upcoming installation of cushioned hardwood flooring.
(20131122-0941)

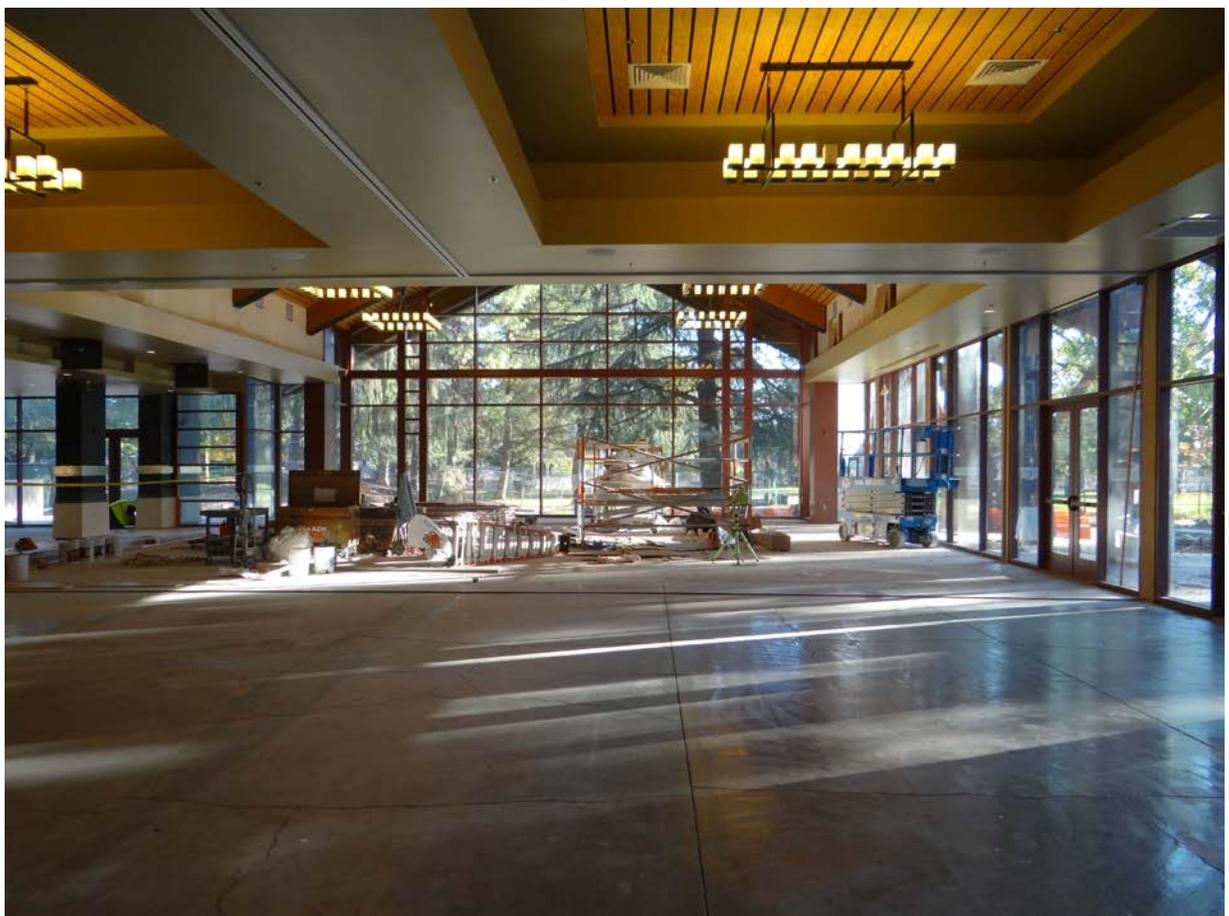



A motorized projection screen is being installed in the Perera Pavilion.
(20131121-1428)
Below: Looking north in the main lobby – McHale Room and Lobby are divided by the stone clad wall.
(201311-0941)

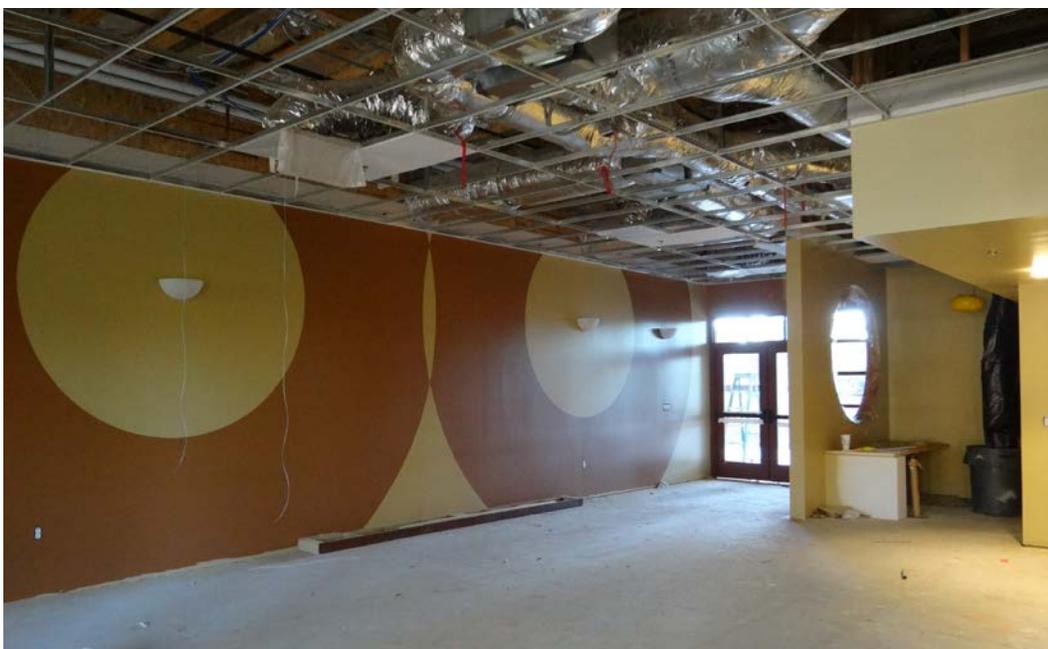

A playful paint scheme is being applied in the Preschool Rooms.
(20131122-0943)

Pleasant Oaks Park

- Sod was installed on the south fields.
- Batting cages and backstops assembly continued.
- Steps and accessible ramp completed on north end of sports building.



View WSW from center walkway – sod now surrounds the infield of this ball field.



View SE from center walkway – sports building and play area across the newly planted grass.



View east from the infield in the first picture above.



View NE from the picnic area on Santa Barbara Road.



Looking north along the west perimeter walkway.



Another set of steps and an accessible ramp have been completed. (North end of the sports building in view.)
