

## Bond Projects Updates for Monday 28 October 2013

### Community Center

- MILESTONE: PG&E primary cables installed and transformer set.
- Wood ceiling finishes installation continued.
- Interior painting, tiling, and electrical installation continued.
- Site work including irrigation, electrical, hardscape, and bioswales continued.
- Casework installation began.




Progress on the installation of laminate flooring as a ceiling finish – main lobby.

(20131022-0822)

Grading, base rock and compaction work for the main entry walkway. Brackets for a bench on the feature wall seen here.

(20131024-0920)

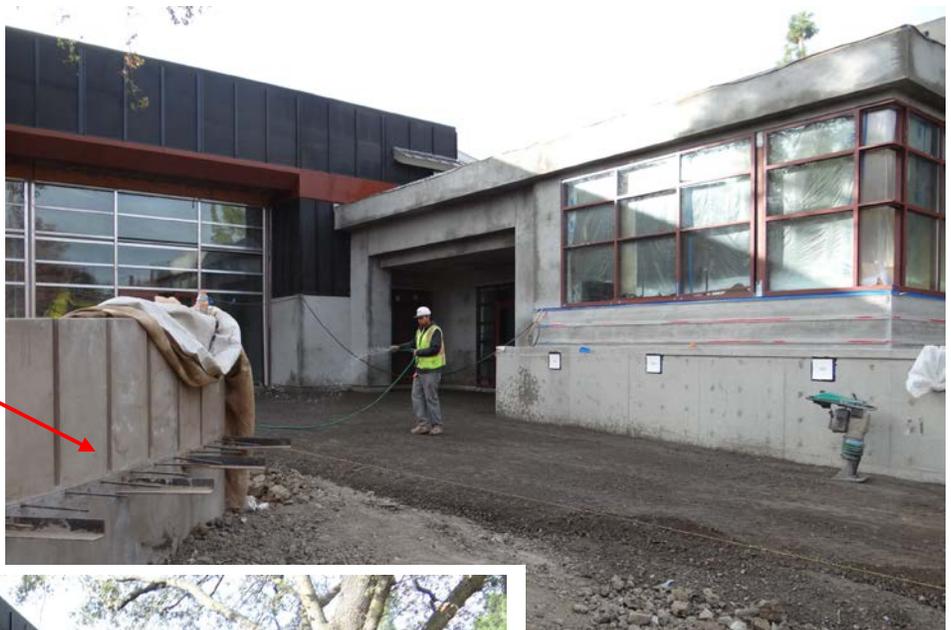

Another view of preparation for finished walkway at the main building entrance. Preschool Rooms entrances are separate from the main entry.


(20131024-0921)



Looking NE at the building – finish stucco coat has been applied to the classrooms. (20131024-0929)



Douglas Fir slats are installed over the acoustic paneling in the Dance Studio. This will be the finish ceiling.  
(20131024-0949)

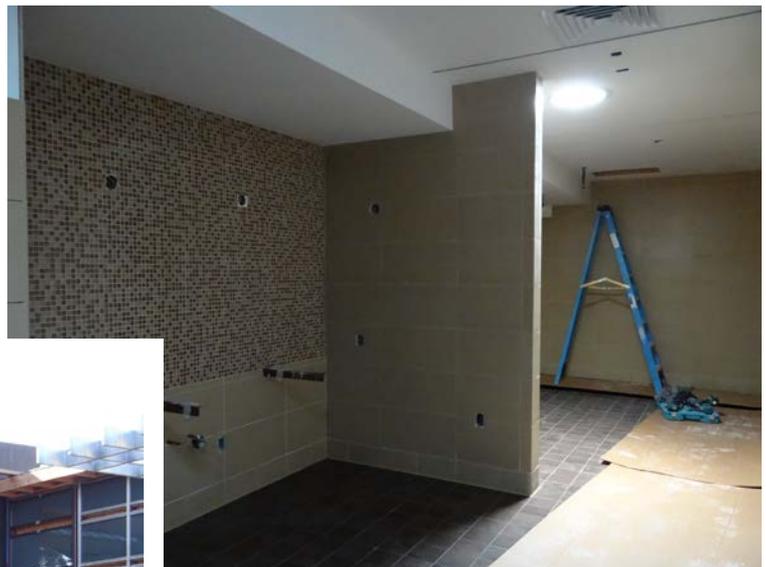

Above: tiling continued in the restrooms. (20131024-0950)



Left: PG&E set the transformer. Power-up scheduled for the new week.

(20131025-1050)

Pleasant Oaks Park

- MILESTONE: Fencing fabric installation complete (awaiting high netting installation).
- Tree plantings continued.
- Playground structure installed – awaiting installation of swings.
- Fields 3 and 4 infield mix completed.
- Shade structure fabric was installed.



The new play structure installation.



This bench was installed in the play structure area.

A fabric shade structure was installed over the new picnic area on Monticello.



Above: Fencing fabric (chain-link) installed on the field bordering the parking lot on Monticello. Netting will be installed above the fencing to keep ball play safely within the park. (20131024-1634)

Right: Chinese Pistach trees were planted along the Santa Barbara perimeter of the newly-fenced playing field.

