

Bond Projects Updates for Monday 2 December 2013

Community Center

- Soil amendment installed in preparation for landscape planting.
- Continued work on irrigation installation (by Park Maintenance and contract services).
- Construction of Preschool Playground chain-link fencing began.
- Installation of data cabling, lighting, electrical, and cabinetry continued.
- Installation of hardwood flooring continued and vinyl floor covering began.
- Finish coat stucco application continued.
- Site work: repair areas were prepared for concrete curb and gutter construction.
- Window framing cover plates and Trespa panels installation continued.



Workers apply stucco finish coat in the preschool entryway. Plastic sheeting protects the newly installed colored concrete.

(20131126-0945)


Soils are nearly planting-ready. The arcade of columns awaits its Trespa panels and trim paint.

(20131127-1240)




Window framing finish plates are being installed, while other trims and joints finishes are also being accomplished.

(20131127-1241)

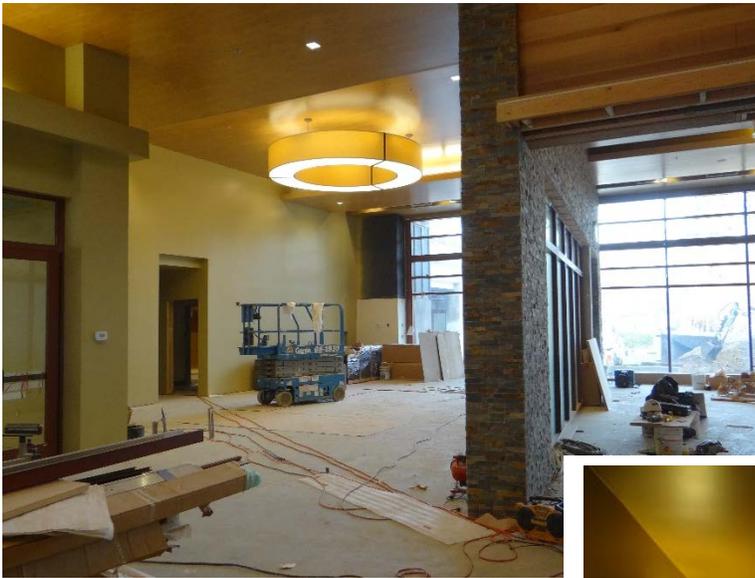

A large custom light fixture installed in the main entry lobby.
(20131126-0959)

View into the events area from the "Flex Storage" where a bar or other service can be set up during events. (20131126-1004)

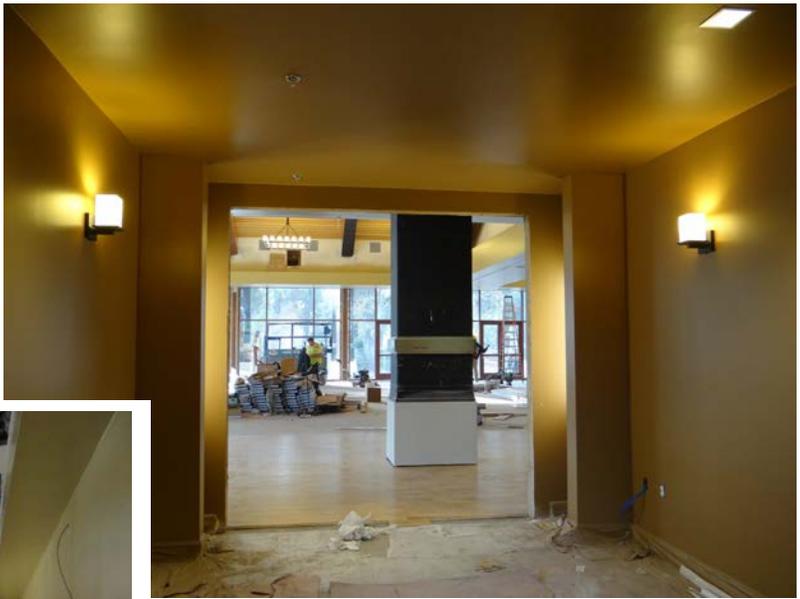

Classroom cabinetry installed and lighting & cabling work proceeding. (20131126-1336)

Solid wood framing for the upcoming mirror installation on the north Dance Studio wall.
(20131126-1338)





Window frame finish panel installation & hardwood border installation in the Dance Studio and Perera Pavilion.
(20131126-1339)

Pleasant Oaks Park

- **MILESTONE: Installation of sod completed.**
- Improvements to sidewalk and curb & gutter.
- Batting cage chain-link fabric installed.
- Backstop frames assembly continued.
- No-mow grasses installed in swales.



Left: "no-mow" grasses being planted in slopes and in swales.
Above: New sod between the sports building and the picnic/batting cages area along Monticello.



View south along the new batting cages.



Freshly poured sidewalk SW corner on Santa Barbara.



Looking NNE from the park center across the newly installed playing fields sod.



Looking NNW across the newly installed sod, now enjoying its irrigation.
