

Bond Projects Updates for Monday 4 November 2013

Community Center

- Operable walls installed in Dance Studio and classrooms.
- Site work continued – curb and gutter, walkways, seat walls, and irrigation.
- MILESTONE: PG&E transformer powered up 10/25/2013
- Interior lighting, data cabling, and electrical installation continued.
- Granite sculpture feature installed at east end patio area.
- Perera Pavilion ceiling-finish installation progressed.

Operable wall in stowed position. It will divide the Perera Pavilion from the Dance Studio.

Slab has been sealed for upcoming floor covering installation.

(20131029-1441)

Below: Stowed operable wall which will divide the Dance Studio into two rooms.

(201310291442)





Left: NW corner of building. Formed section of walkway connecting the west side walkway to the front walkway.

(20131031-0958)




Above and left: Forms for seat walls and for curb and gutter along the front of the building.

(20131031-0959 & 1000)

Curb and gutter concrete being poured, while workers install rebar for the flatwork in several areas around the building.

(20131101-1113)



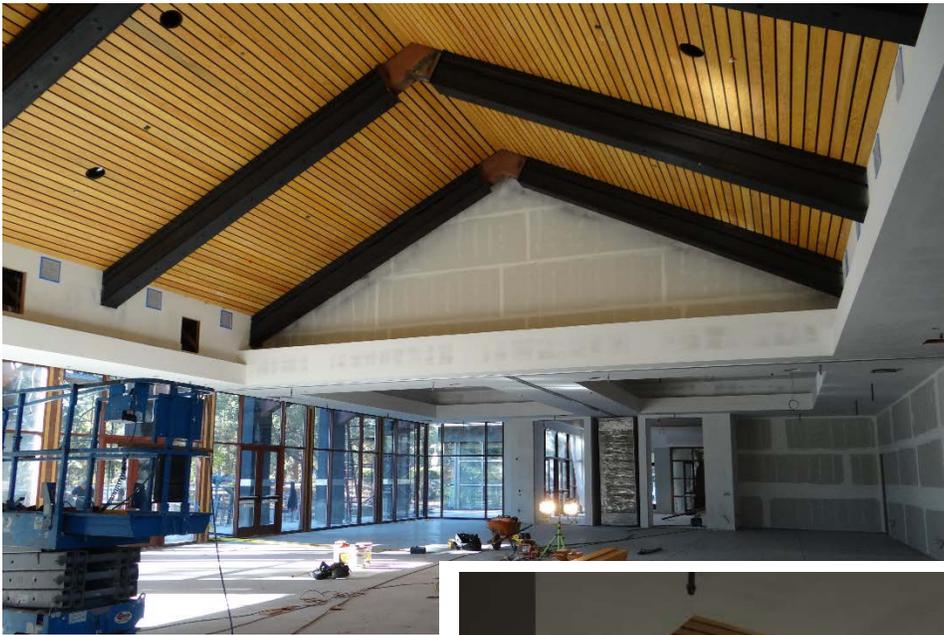

Progress on the finish ceiling installation in the Perera pavilion. (20131031-1013)

Looking out the main events entry lobby. A patio will be poured in the area seen out the windows on the right. (20131101-1121)



Looking east through the preschool playground. Offices at left and classrooms straight ahead. (20131101-1128)

Pleasant Oaks Park

- Bleacher seating installation began.
- Redwood trees were planted and beds mulched.
- Picnic tables delivered to site and placement in designated areas began.
- Shade tops on the dugouts are being installed.
- Final grading accomplished on 2 more playing fields.
- Play area DG (decomposed granite) has been compacted & swings installed on play equipment.

Material around the play structures has been compacted.



Left: Bleacher seating is being installed near the dugouts.
Below: Workers installing shade roofing on the dugout at the right. Field preparation continues.





Left: View from a dugout with the shade top completed.
Below: Redwood trees were planted and mulched along the west side of the park.



Tables have been placed in the SW corner picnic area. BBQ equipment will be installed on the posts & frames.
