

Bond Projects Updates for Monday 2 September 2013

Community Center

- Standing seam metal roofing material installation continued.
- Progress on preschool playground site work, forms, drainage, and rebar work.
- CCWD installed the water supply backflow preventer for service.
- PGE transformer pad was reset over repaired conduits. Gas line installation continued.
- Existing asphalt and concrete paving and curbs demolished for site improvement work.
- Concrete poured for east feature wall, south seat wall, and west filter planter.
- West side walkway grading and layout work proceeded.
- Interior: sheetrock work continued.



On Tuesday, concrete was pumped into the south seat wall from a truck near the front (north) entrance.

(20130827-0803)

By Friday, the forms had been removed, revealing the stepped seat wall around the Hackberry tree.

(20130830-1451)




Transformer pad. Compaction over gas line. Water service black-flow preventer. (20130830-1442)



Colored concrete feature wall east of the main events entry.
(20130830-1447)

Graded, compacted pad for upcoming walkway, seating area, landscape beds at east side of events rooms.
(20130830-1447)

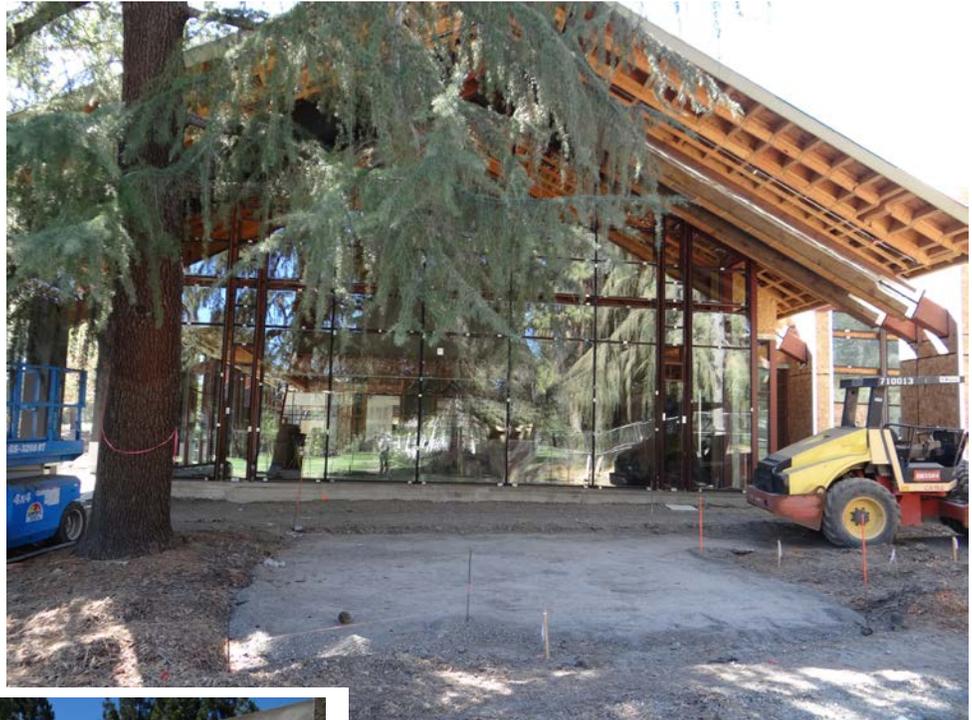

The new planting beds and flatwork layout and rebar work in the Preschool playground.
(20130830-1453)



View north of playground, showing where the new and existing features adjoin.
(20130830-1456)

View south along the west side – pathway connecting preschool classrooms’ “back doors” with the access pathway to the shared playground.
(20130830-1458)



Pleasant Oaks Park

- Irrigation valve boxes installed.
- Pathway compaction and layout continued.
- Permitting agencies’ required filter fabric installed at parking lot drive entry (photo below).

