

## Bond Projects Updates for Monday 6 August 2012

### Senior Center


- Concrete was poured in the mid-section of the east side meandering walkway.
- Forms were added for another section of walkway, which will eventually span the park from Gregory Lane to the north end near Patricia Drive.
- The ventilation hood was installed over the future cooking surfaces areas in the large kitchen.
- The exhaust fan hood was installed over the future dishwasher.
- Mechanical, electrical, and plumbing work continued.
- Sheetrock installation is nearing completion, while taping continues.
- Stucco finish coat work proceeded.
- **Senior Center Standard Furniture Package bids** were opened Friday July 27, 2012 at 10:00am at the District Office. The results are currently being verified and will be considered by the Board at the regular Bond Projects segment of the Board Meeting on August 8, 2012 at 6:00pm.

Right: The exhaust hood over the dishwasher area. (20120801-1709)

Below: The ventilation hood over the cooking appliance area. (20120801-1711)



Right: Main electrical circuit panels – many wire runs are already pulled through the building. (20120801-1709)

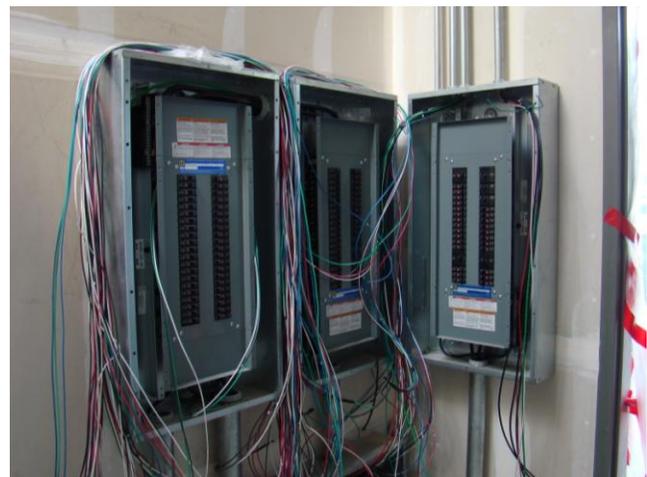



The Multi-Purpose Room is taped and awaiting painting. (20120801-1711)



Two views of the fireplace and adjoining media storage cupboards in the Library/Lounge. (20120801-1718)

Teen Center

- Mechanical, electrical, and plumbing work continued.
- Main room lighting was installed and tested on temporary power.
- Vinyl-backed ceiling insulation was buttoned up.
- Cabinetry and counter installation continued.



Left & Below:  
Electricians installed  
and tested the new  
main room lighting.

The vinyl-backed  
insulation has been  
“buttoned” to the  
ceiling.

(20120731-1151&1155)



Completed assembly of the  
cubbies and lockers near the  
front entrance.

(20120803-1727)





Assembled games cupboard at the north end of the main room. The flat screen display for gaming will be on the wall to the right of the cupboard. (20120731-1156)

Counters and cupboards in the Storage/Office space to the east near the front entry. (20120731-1156)



Current view south from the games area. (20120803-1730)

Community Center

- Notice to Proceed will be issued to DL Falk in early August 2012.

Pleasant Oaks Park (POP)

- A project design presentation will be given by architect Phil Abey to the District Board at a Board Study Session on Monday 8/20/2012 at 9:00am at the District Office (147 Gregory Lane, PH).
